APPENDIX G

Project Schedule

Miniota Lagoon Design Project
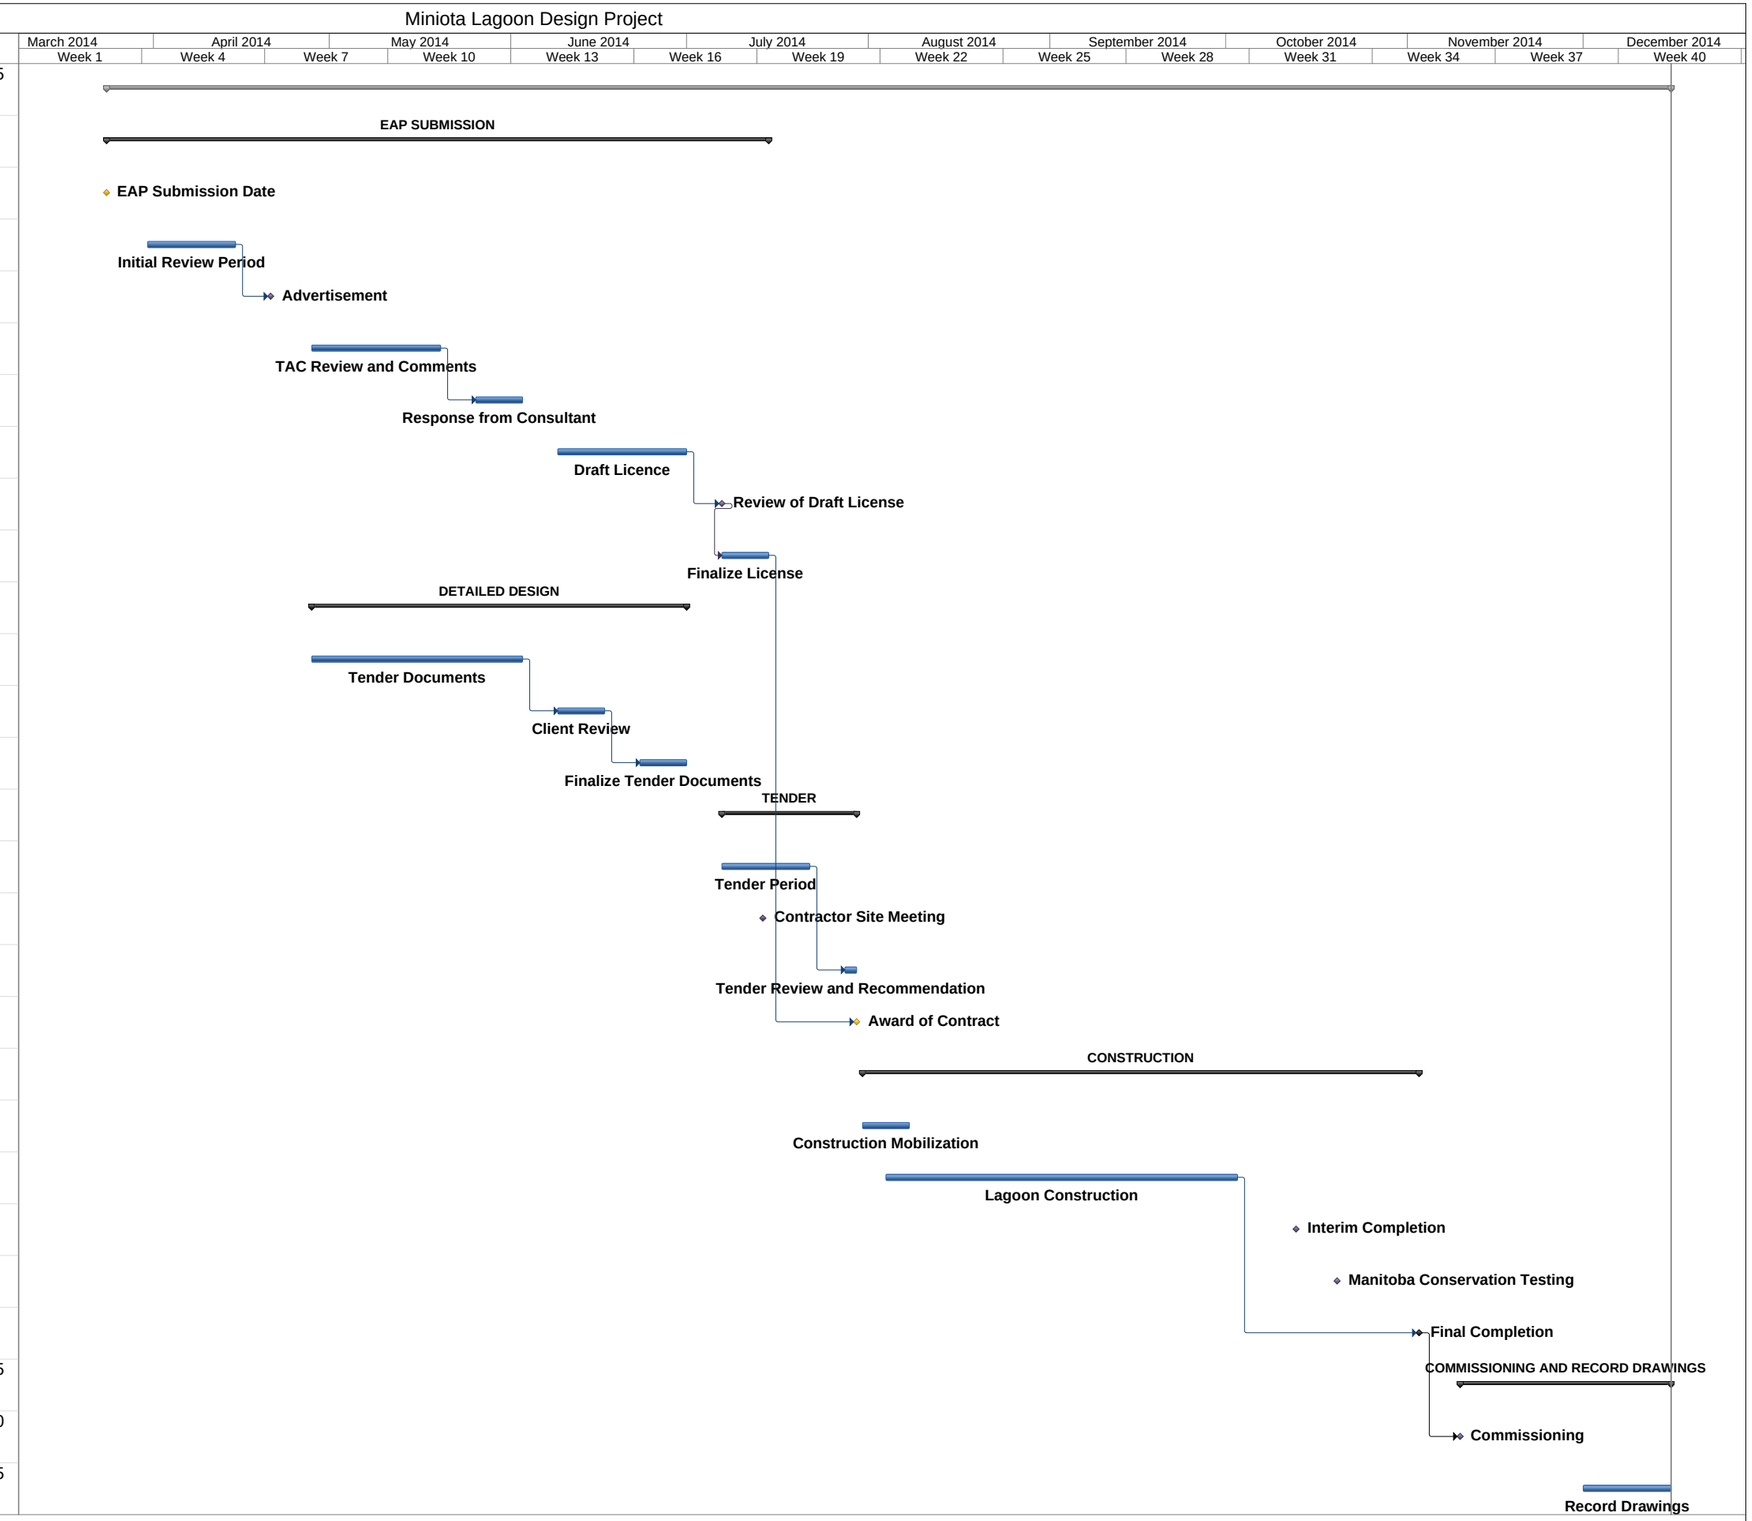
ID	Task Name	Duration	Start	Finish
0	Miniota Lagoon Design Project	267 days	March 24	December 15
1	1 EAP SUBMISSION	113 days	March 24	July 14
2	1.1 EAP Submission Date	0 days	March 24	March 24
3	1.2 Initial Review Period	15 days	March 31	April 14
4	1.3 Advertisement	0 days	April 21	April 21
5	1.4 TAC Review and Comments	22 days	April 28	May 19
6	1.5 Response from Consultant	8 days	May 26	June 2
7	1.6 Draft Licence	22 days	June 9	June 30
8	1.7 Review of Draft License	0 days	July 7	July 7
9	1.8 Finalize License	8 days	July 7	July 14
10	2 DETAILED DESIGN	64 days	April 28	June 30
11	2.1 Tender Documents	36 days	April 28	June 2
12	2.2 Client Review	8 days	June 9	June 16
13	2.3 Finalize Tender Documents	8 days	June 23	June 30
14	3 TENDER	23 days	July 7	July 30
15	3.1 Tender Period	15 days	July 7	July 21
16	3.2 Contractor Site Meeting	0 days	July 14	July 14
17	3.3 Tender Review and Recommendation	2 days	July 28	July 29
18	3.4 Award of Contract	0 days	July 30	July 30
19	4 CONSTRUCTION	95 days	July 31	November 3
20	4.1 Construction Mobilization	8 days	July 31	August 7
21	4.2 Lagoon Construction	60 days	August 4	October 2
22	4.3 Interim Completion	0 days	October 13	October 13
23	4.4 Manitoba Conservation Testing	0 days	October 20	October 20
24	4.5 Final Completion	0 days	November 3	November 3
25	5 COMMISSIONING AND RECORD DRAWINGS	36 days	November 10	December 15
26	5.1 Commissioning	0 days	November 10	November 10
27	5.2 Record Drawings	15 days	December 1	December 15
